



ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Nov 6, '16					
							T	F	S	S	M	T
1	MOBILIZATION	7 days	Thu 11/10/16	Fri 11/18/16		MOBILIZATION						MOBILIZA
2	E&S	2 days	Wed 11/16/16	Thu 11/17/16		E&S						
3	SITE & TREE FENCING	5 days	Thu 11/10/16	Wed 11/16/16		SITE & TREE FENCING						SITE & TREE FEN
4	LAYOUT	58 days	Fri 11/11/16	Tue 1/31/17		LAYOUT						
5	CLEARING & GRUBBING	4 days	Fri 11/18/16	Wed 11/23/16		CLEARING & GRUBBING						
6	DEMOLITION	12 days	Thu 11/17/16	Fri 12/2/16		DEMOLITION						
7	STRIP TOPSOIL	54 days	Tue 11/22/16	Fri 2/3/17		STRIP TOPSOIL						
8	SITE CUT/FILL	60 days	Mon 11/28/16	Fri 2/17/17		SITE CUT/FILL						
9	RAIN GARDENS	28 days	Wed 11/30/16	Fri 1/6/17		RAIN GARDENS						
10	EXPORT	45 days	Wed 11/30/16	Tue 1/31/17		EXPORT						
11	SANITARY SEWER	5 days	Mon 12/12/16	Fri 12/16/16		SANITARY SEWER						
12	STORM SEWER	60 days	Mon 11/28/16	Fri 2/17/17		STORM SEWER						
13	DOMESTIC WATER	5 days	Mon 12/19/16	Fri 12/23/16		DOMESTIC WATER						
14	CONCRETE	8 days	Wed 3/1/17	Fri 3/10/17		CONCRETE						
15	PAVING	15 days	Mon 3/13/17	Fri 3/31/17		PAVING						
16	STRIPING/SIGNAGE	2 days	Thu 3/30/17	Fri 3/31/17		STRIPING/SIGNAGE						
17	BASKETBALL COURT RE-SURFACE	23 days	Wed 3/1/17	Fri 3/31/17		BASKETBALL COURT RE-SUF						
18	TENNIS COURT RE-SURFACE	23 days	Wed 3/1/17	Fri 3/31/17		TENNIS COURT RE-SURFACE						
19	POROUS PATH	85 days	Mon 12/5/16	Fri 3/31/17		POROUS PATH						
20	LANDSCAPING	23 days	Wed 3/1/17	Fri 3/31/17		LANDSCAPING						
21	FINISH FENCING	80 days	Mon 12/12/16	Fri 3/31/17		FINISH FENCING						
22	PLAYGROUND EQUIPMENT	30 days	Mon 2/20/17	Fri 3/31/17		PLAYGROUND EQUIPMENT						
23	PLAYGROUND SURFACE	23 days	Wed 3/1/17	Fri 3/31/17		PLAYGROUND SURFACE						
24	SITE SEATING	23 days	Wed 3/1/17	Fri 3/31/17		SITE SEATING						




Project: Clem Macrone Park
Date: 11/28/16

Task		Summary		Split	
Task Progress		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Critical Task Progress		Rolled Up Milestone		Group By Summary	
Milestone		Rolled Up Progress		Deadline	

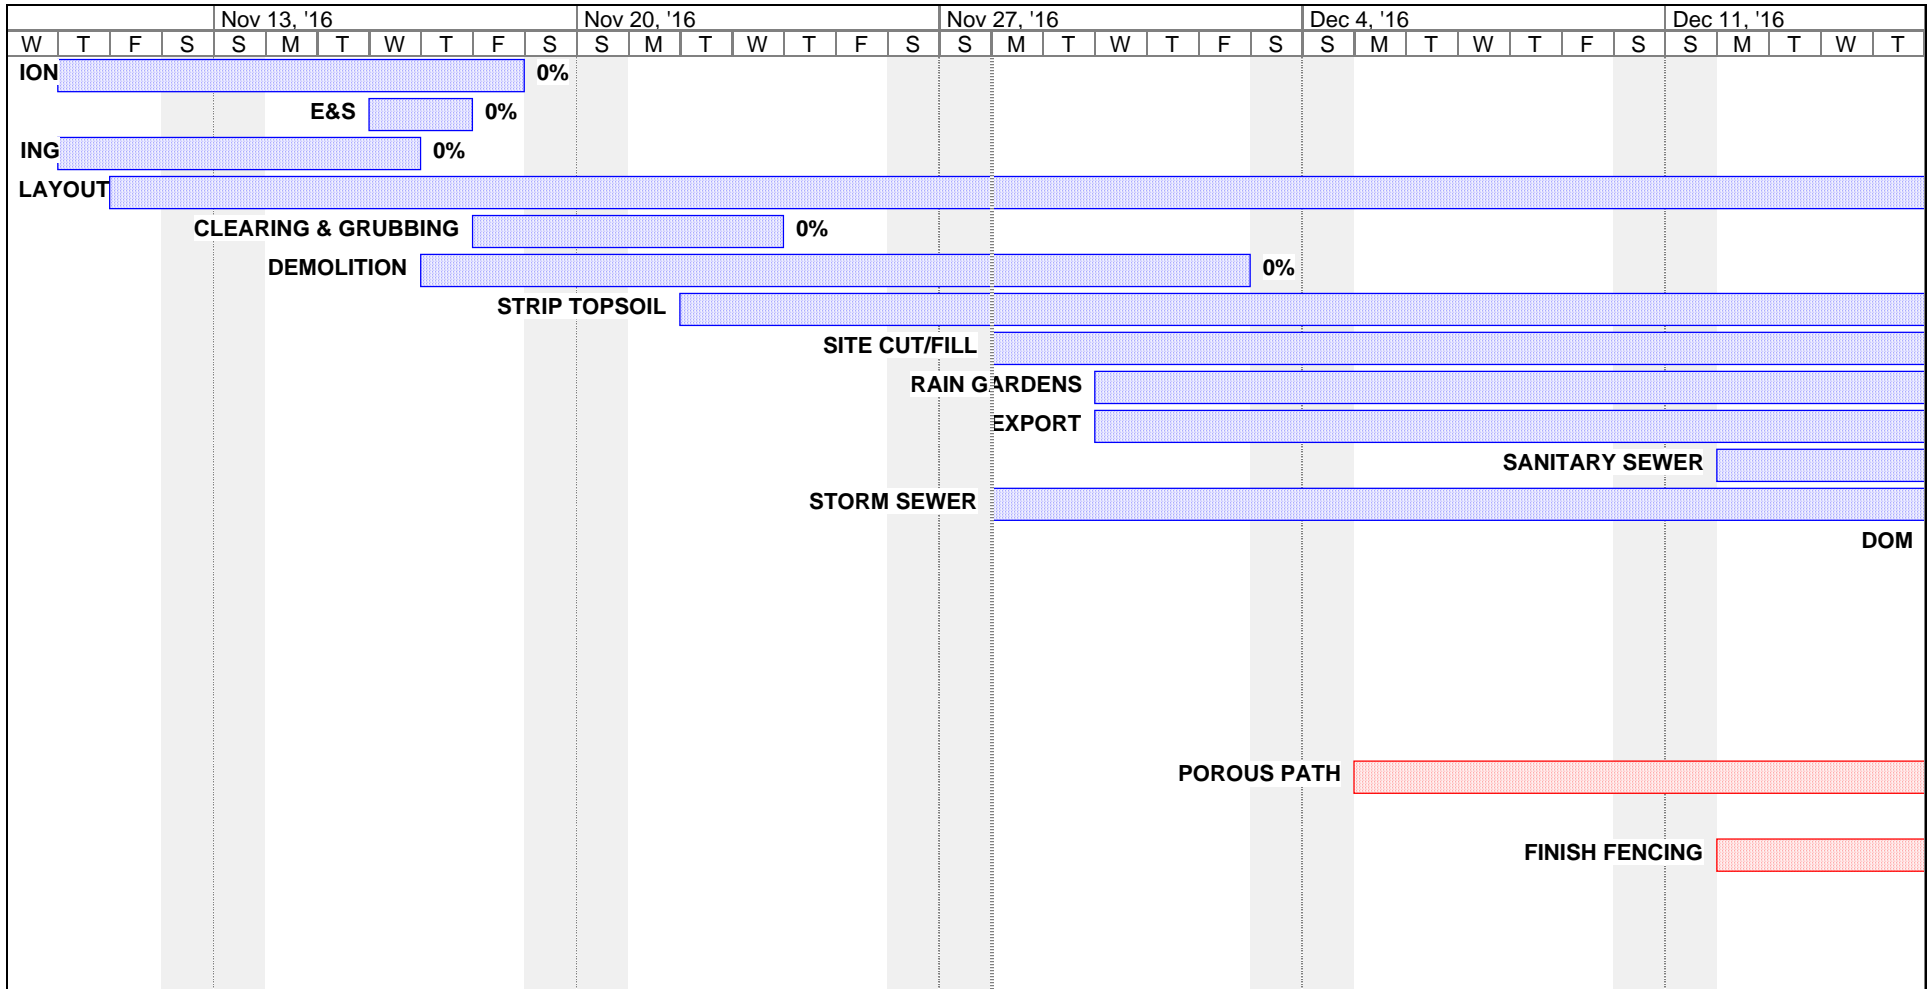


Project: Clem Macrone Park
Date: 11/28/16

Task		Summary		Split	
Task Progress		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Critical Task Progress		Rolled Up Milestone		Group By Summary	
Milestone		Rolled Up Progress		Deadline	

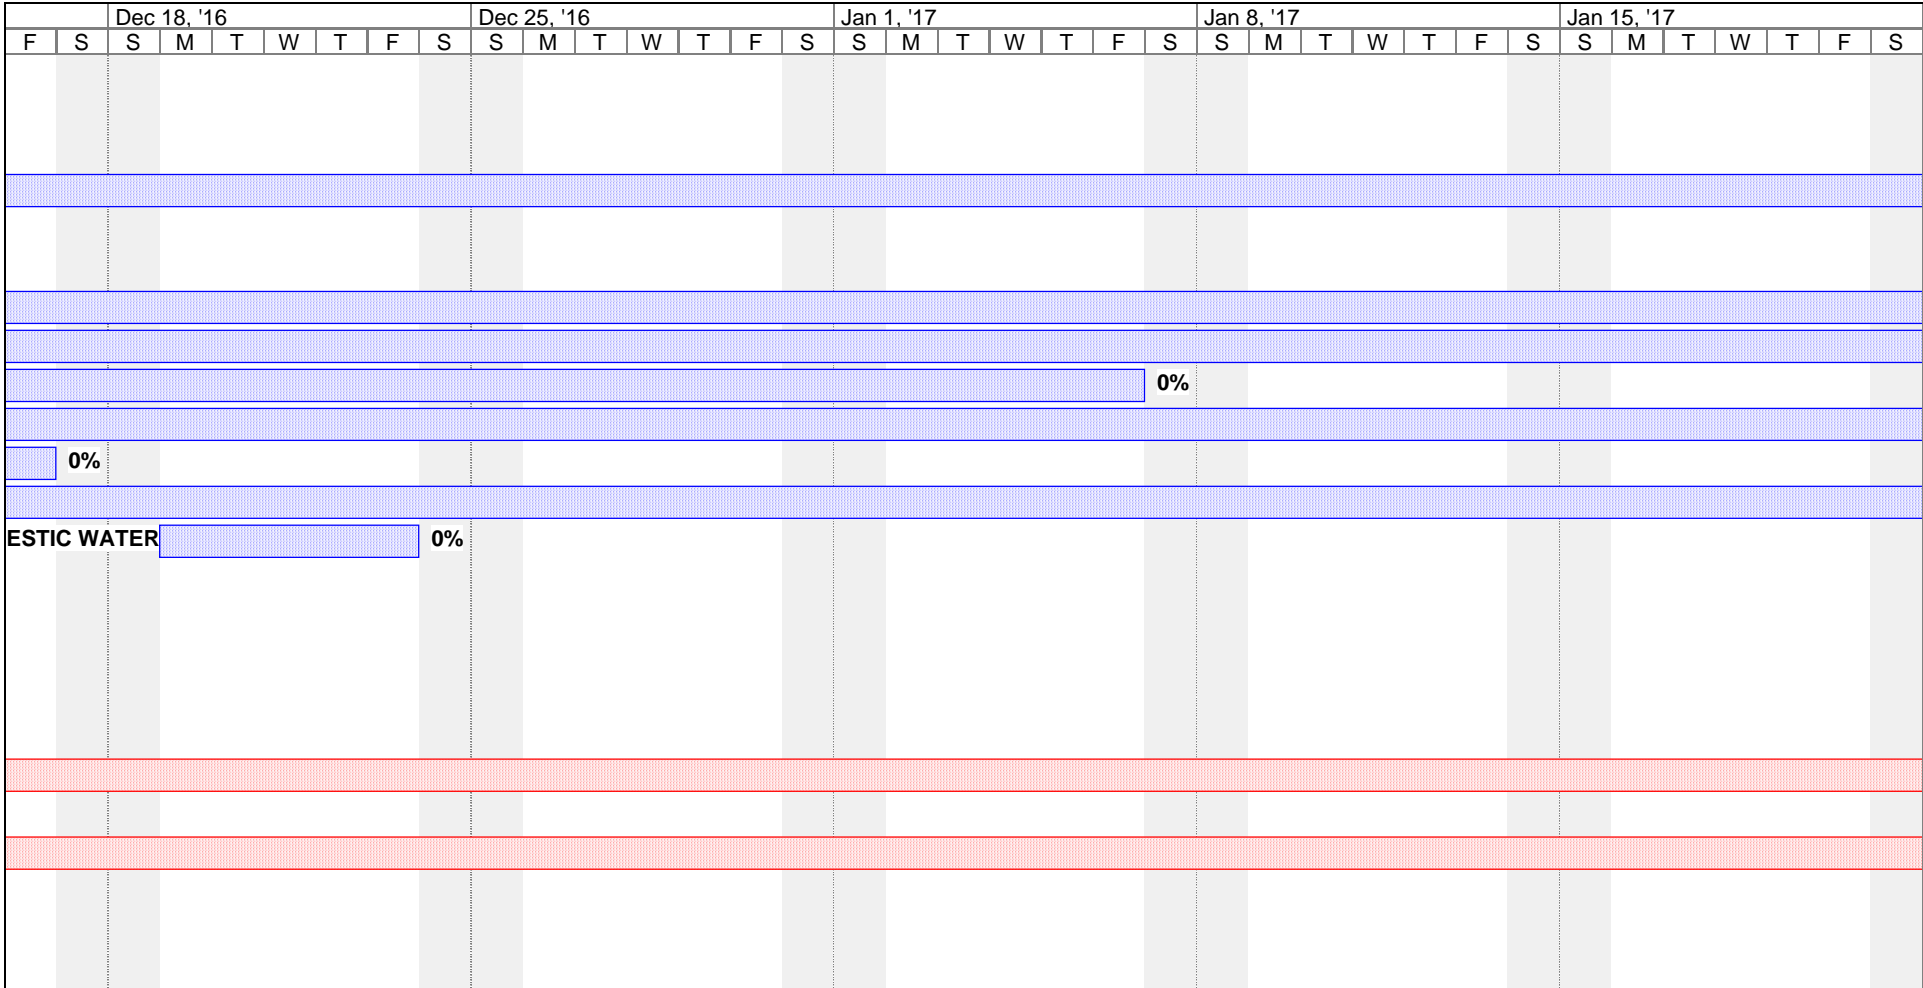

Project: Clem Macrone Park
Date: 11/28/16

Task		Summary		Split	
Task Progress		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Critical Task Progress		Rolled Up Milestone		Group By Summary	
Milestone		Rolled Up Progress		Deadline	

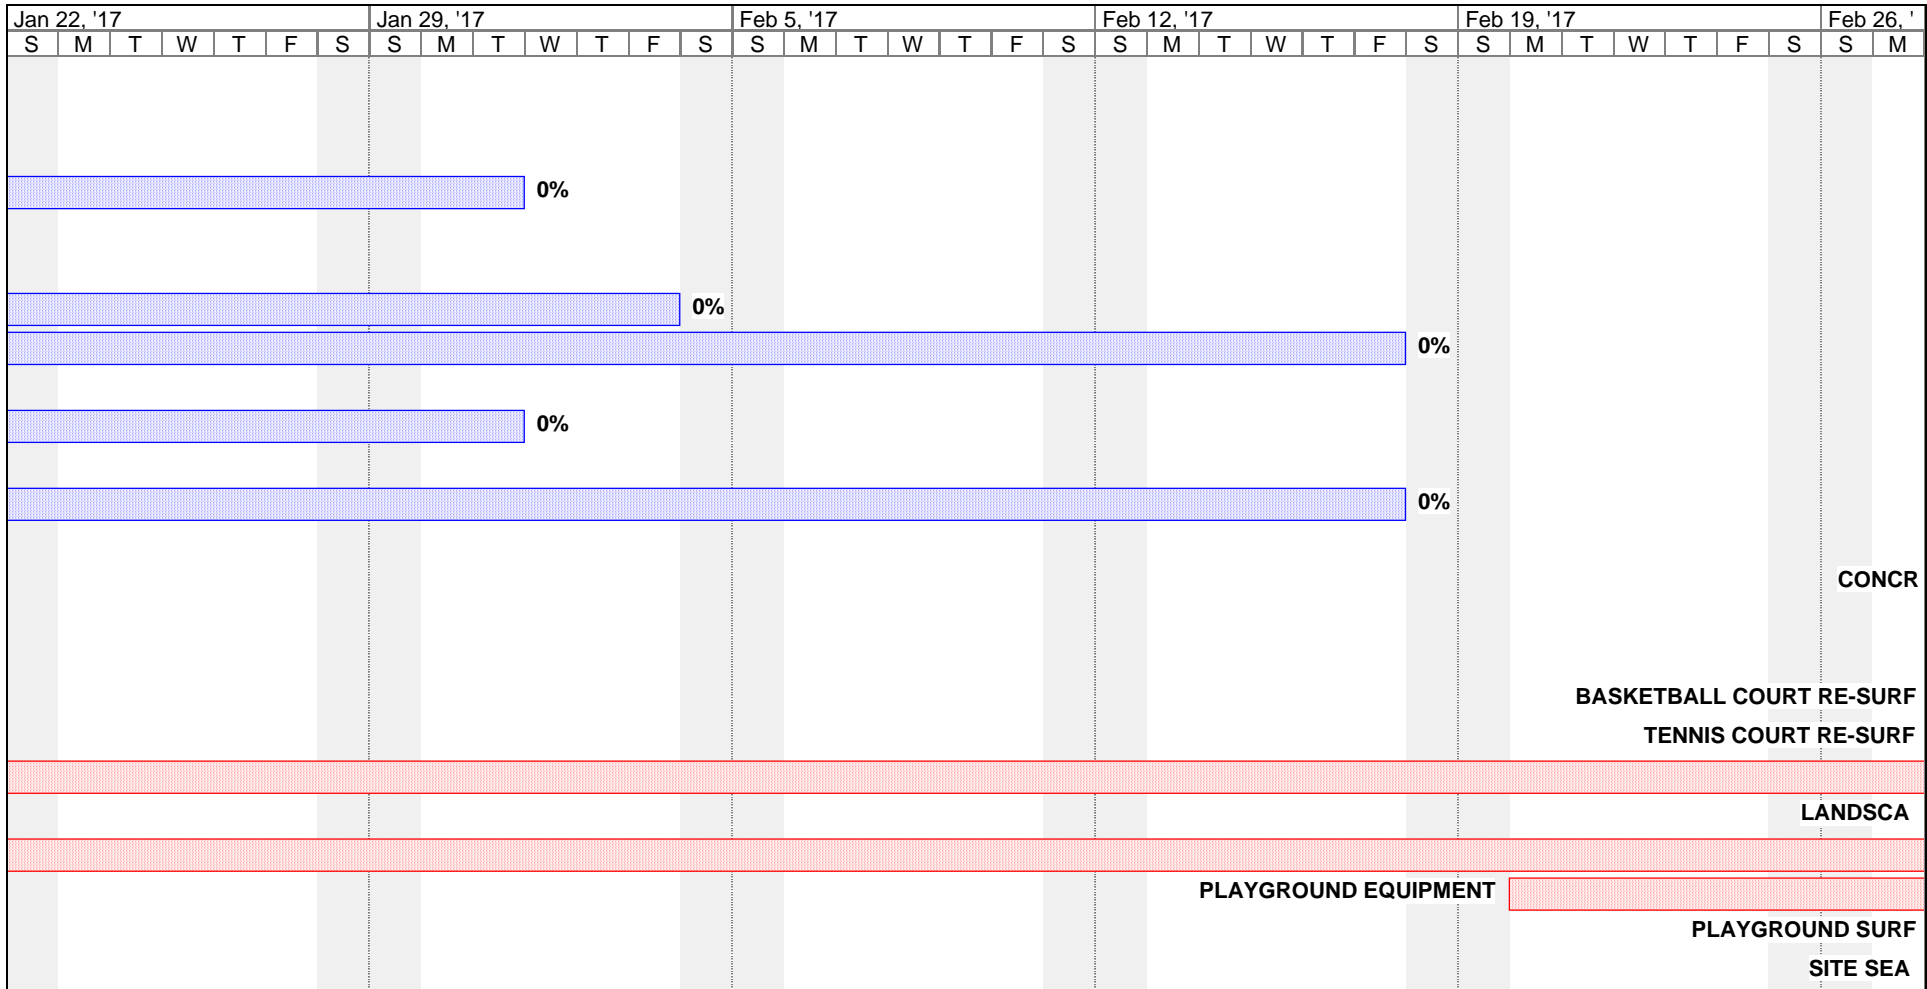

CONCR

BASKETBALL COURT RE-SURF

TENNIS COURT RE-SURF

LANDSCA


PLAYGROUND EQUIPMENT









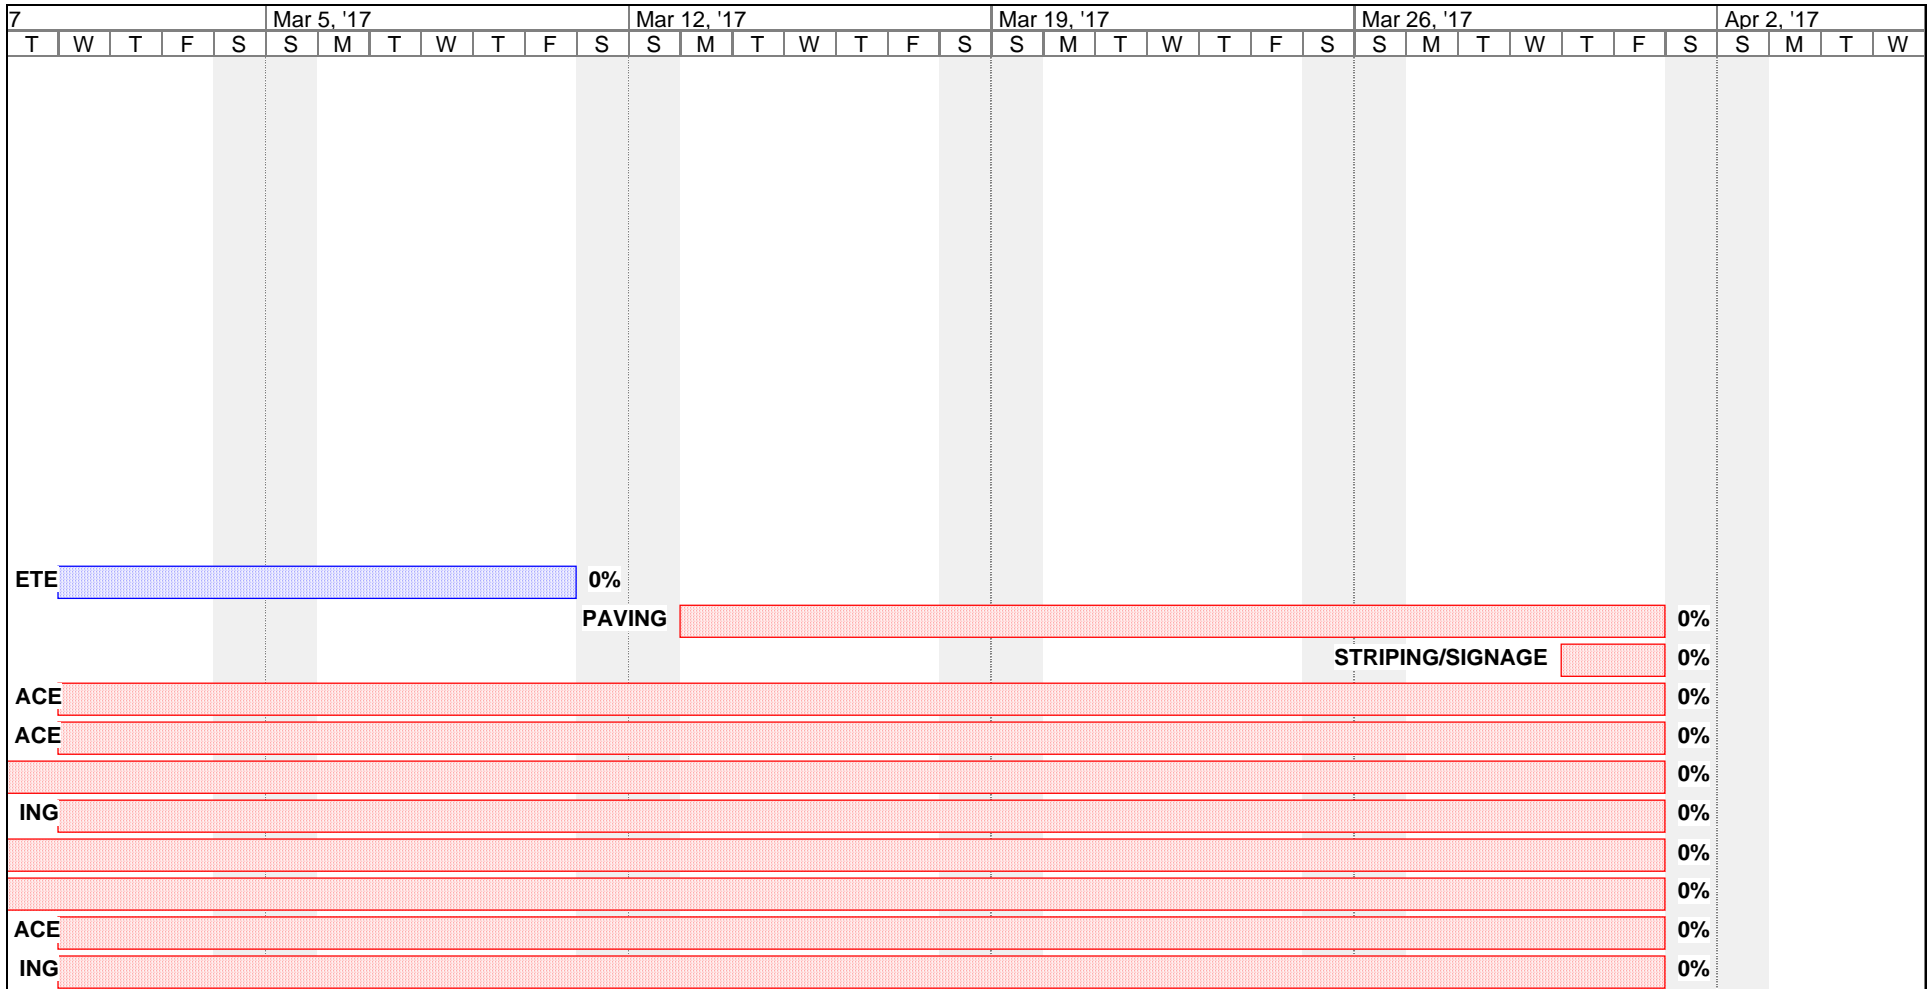





PLAYGROUND SURF

SITE SEA

Project: Clem Macrone Park
Date: 11/28/16

Task		Summary		Split	
Task Progress		Rolled Up Task		External Tasks	
Critical Task		Rolled Up Critical Task		Project Summary	
Critical Task Progress		Rolled Up Milestone		Group By Summary	
Milestone		Rolled Up Progress		Deadline	



Project: Clem Macrone Park Date: 11/28/16	Task		Summary		Split	
	Task Progress		Rolled Up Task		External Tasks	
	Critical Task		Rolled Up Critical Task		Project Summary	
	Critical Task Progress		Rolled Up Milestone		Group By Summary	
	Milestone		Rolled Up Progress		Deadline	
